

MARINA ONE KOCHI

Project Progress Report

30/04/2023





- **Terrace painting completed. Solar panel frame fixing done.**



- **Door fixing completed.**





- **Over Head Tank & Lift Motor Room ladder painting completed**



- **Stepladder above plumbing pipe completed**





Paint first coat completed 16031/19335 sqm

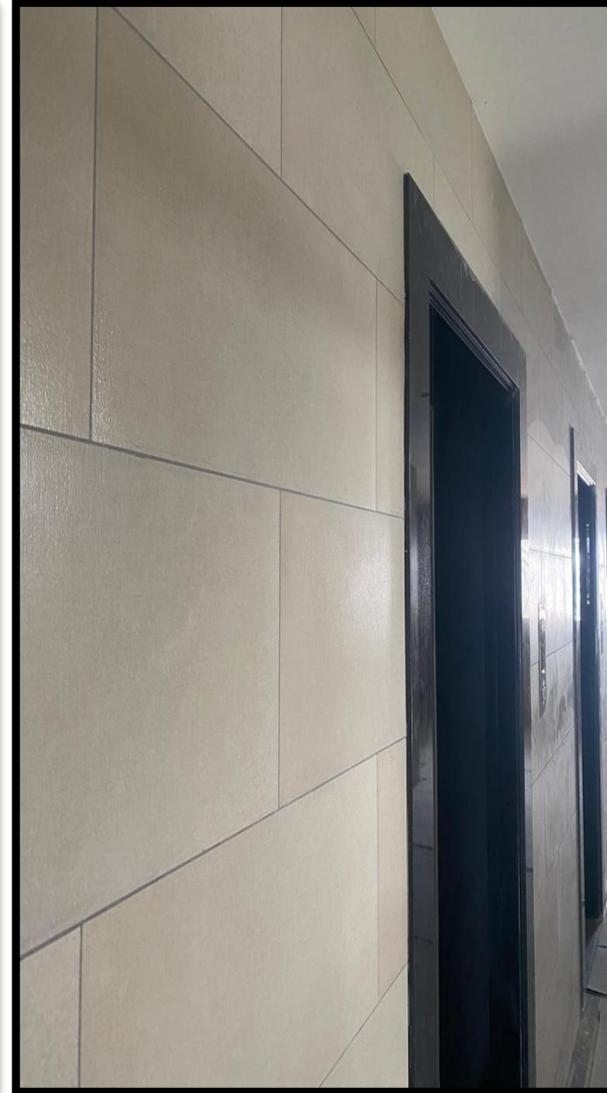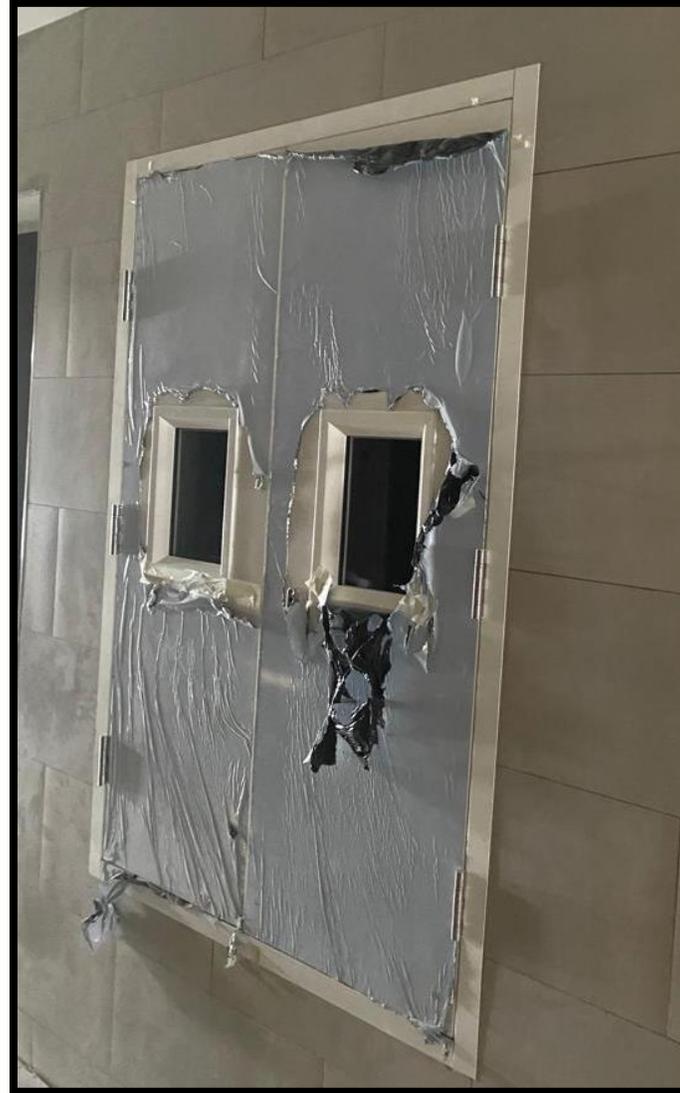

- wall tile grouting 14/28 completed.
- Ceiling paint 1st coat 28/28 floor completed.
- Metal door fixing 18/28 floor completed.

- **SGML glass fixing completed.**
- **Primer & putty touch up works completed.**
- **Texture paint 7/28 floor completed.**

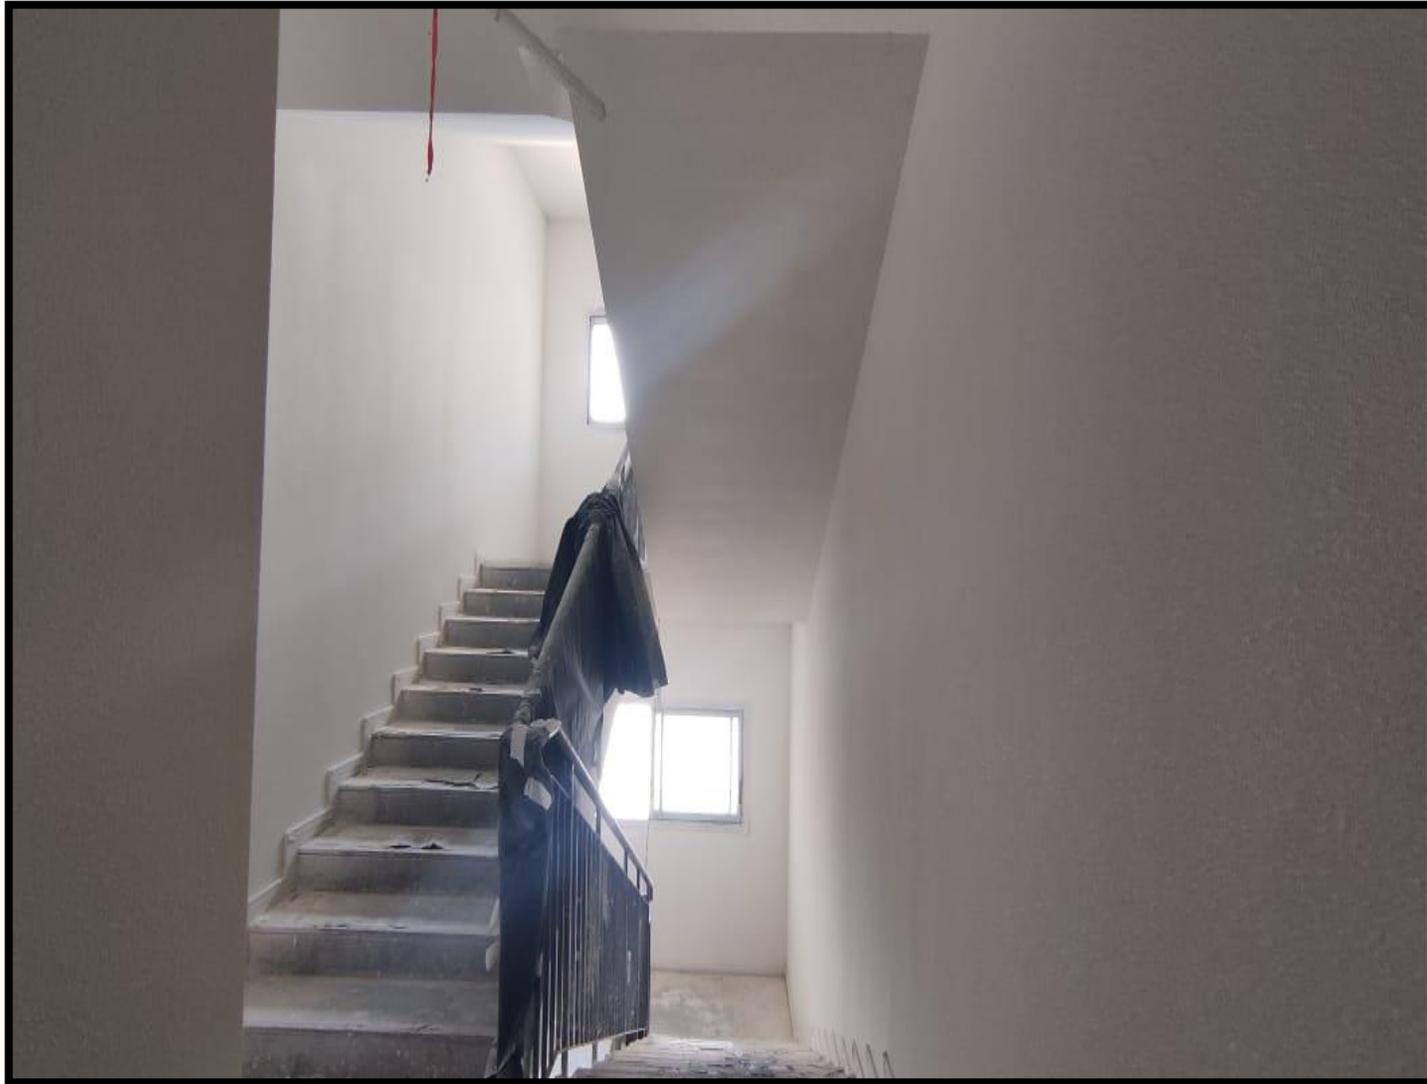

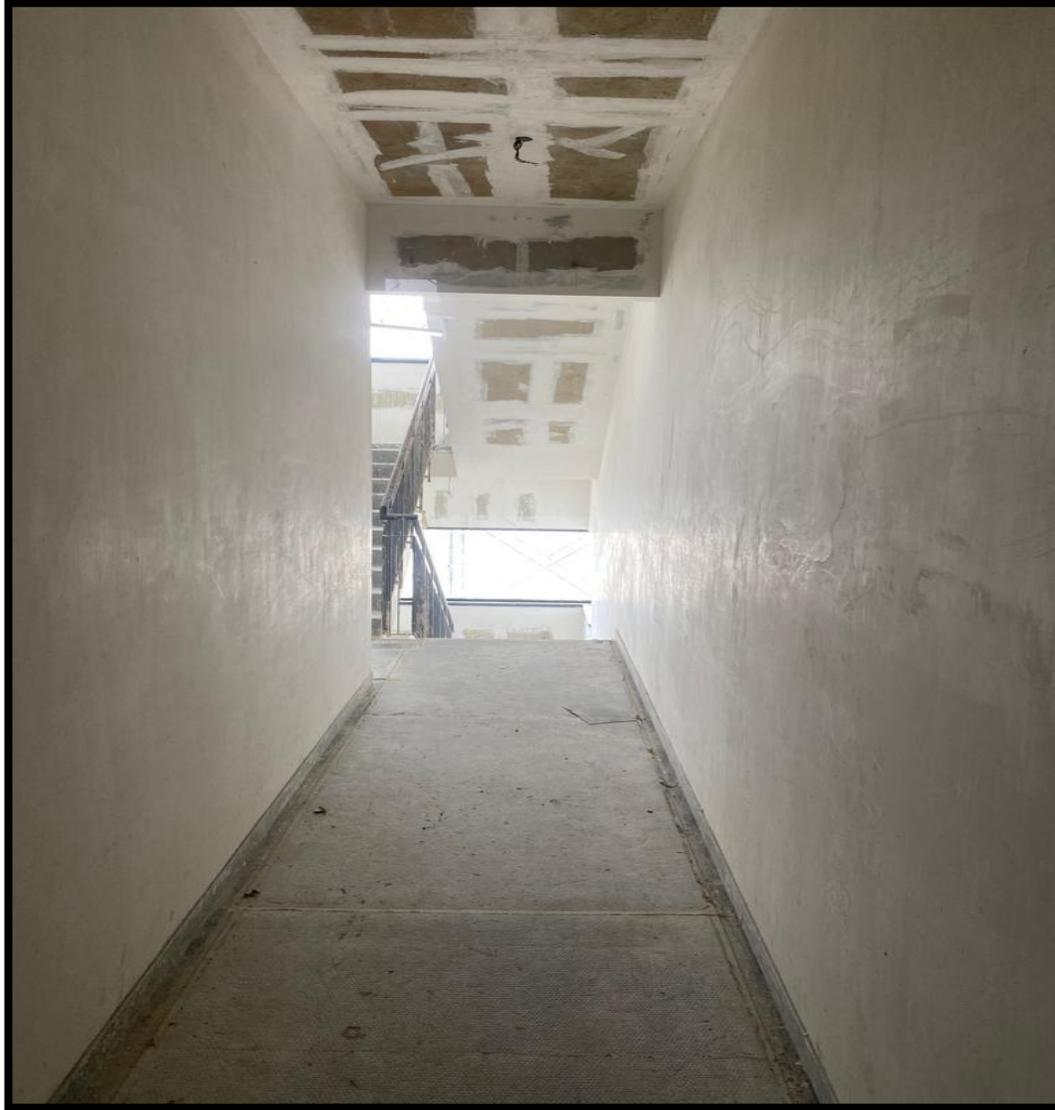

- **Plaster Of Paris & Primer works for painting in progress..**
- **Break open glass 28/28 Floors completed.**




- **Helipad railing works in progress.**



- **Terrace painting completed. Solar panel frame fixed.**



- **Paint first coat completed 11649/13769 sqm**

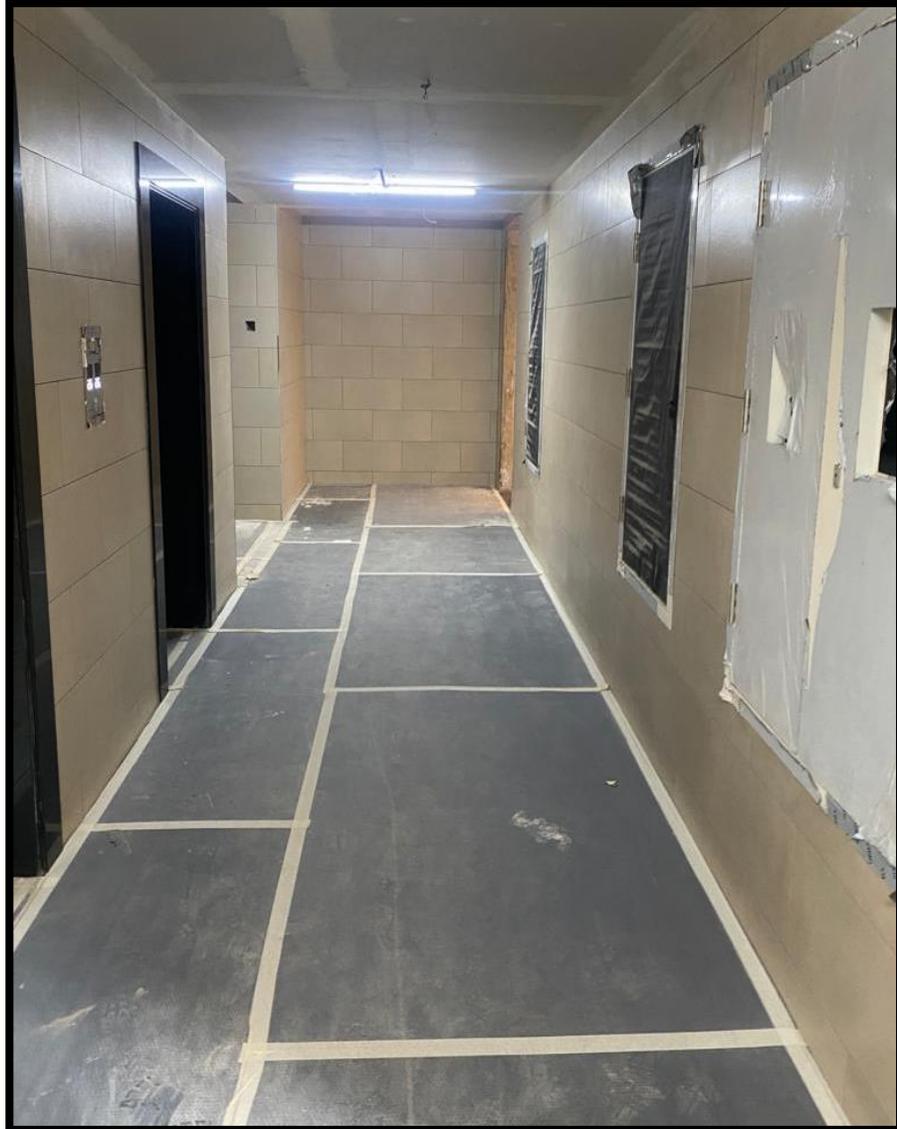

- **Ceiling paint 1st coat 27/27 floor completed**
- **Wall grouting 13/27 Floor completed.**
- **Metal door fixing : 19/27 Floor completed**



- **Gyproc works completed.**
- **SGML glass fixing 27/27 Floor completed.**
- **POP works 27/27 Floor completed.**



- **Plaster Of Paris works for painting completed.**
- **SGML breakopen window 27/27 Floor completed.**
- **Surface preparation & 2 coat primer works in progress**

SOUTH WING-12



Structure completed. Terrace waterproofing & protective screed 2/4 flats completed



SGML works 10 floors in progress

SOUTH WING-12





Toilet Floor Tiling T1-96,T2-98,T3-97/100 flats completed



- **Marble Flooring 99/100 flats completed**

SOUTH WING-12

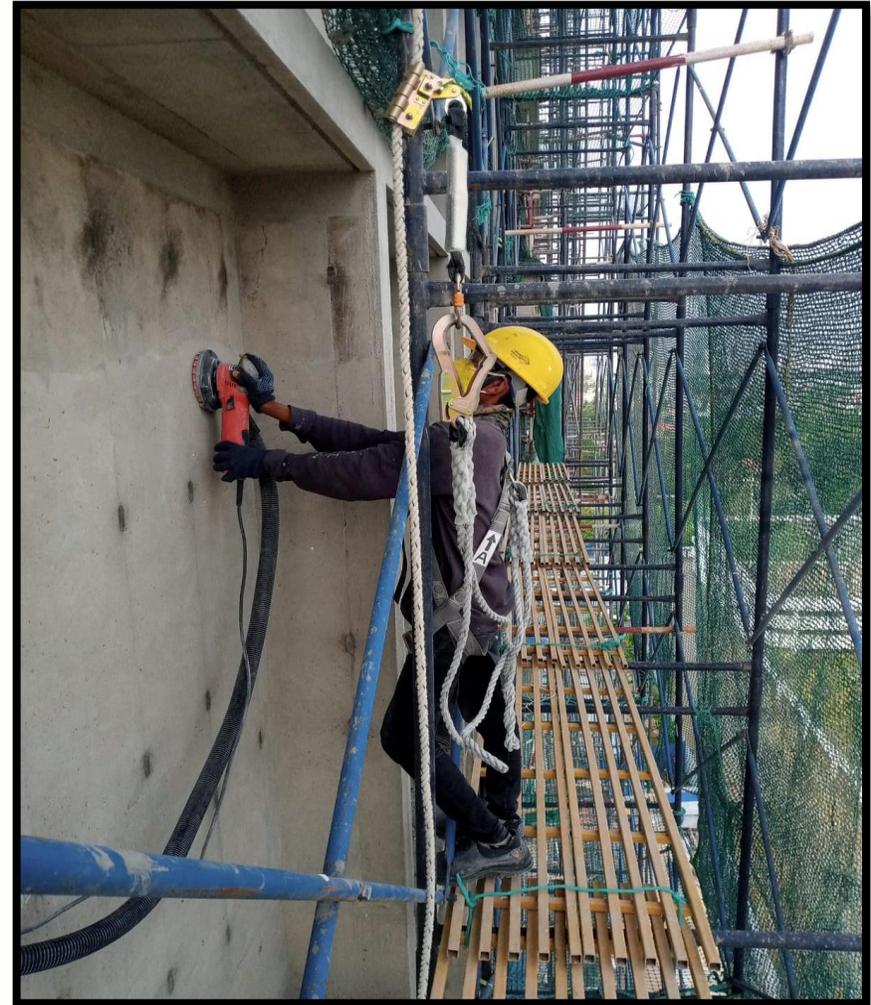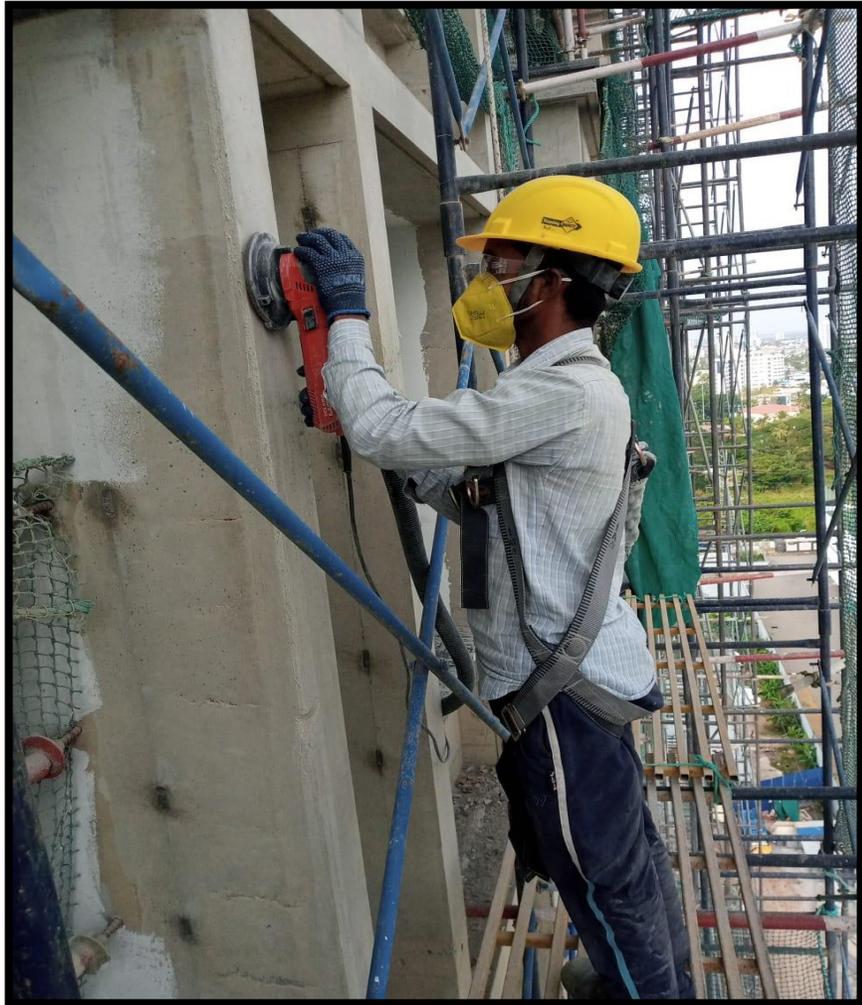

External grinding works in progress

NORTH WING 02



Third floor roof slab casted. Fourth floor roof slab pour 1 reinforcement in progress



Excavation 100% completed. Pile chipping 100% completed. PCC 100% completed. Raft steel works in progress.



900mm Dia Piles:



- Excavation completed - **91 / 204** piles
- Pile chipping completed - **59 / 204** piles

600mm Dia Piles:

- Excavation completed - **12 / 22** piles
- Pile chipping completed - **00 / 22** piles



Vacuum Dewater Flooring 97% completed

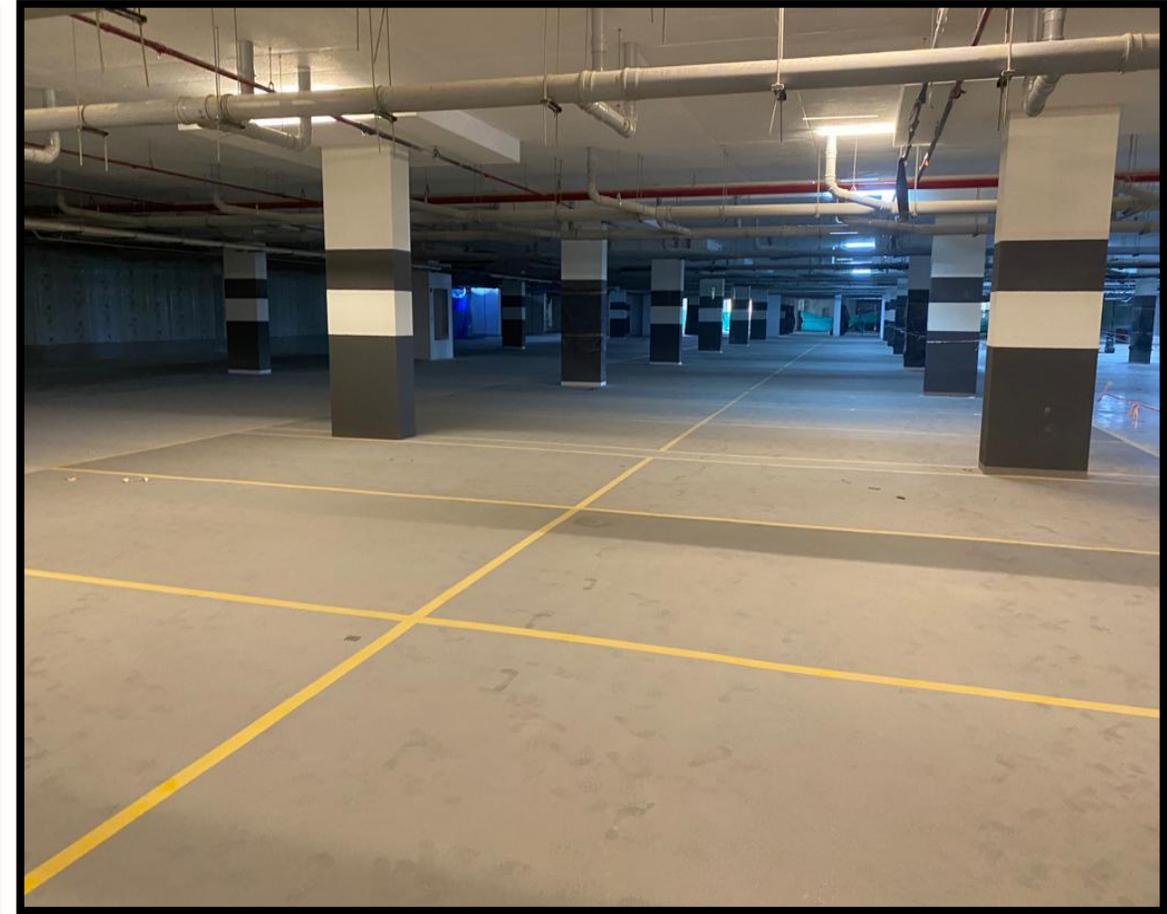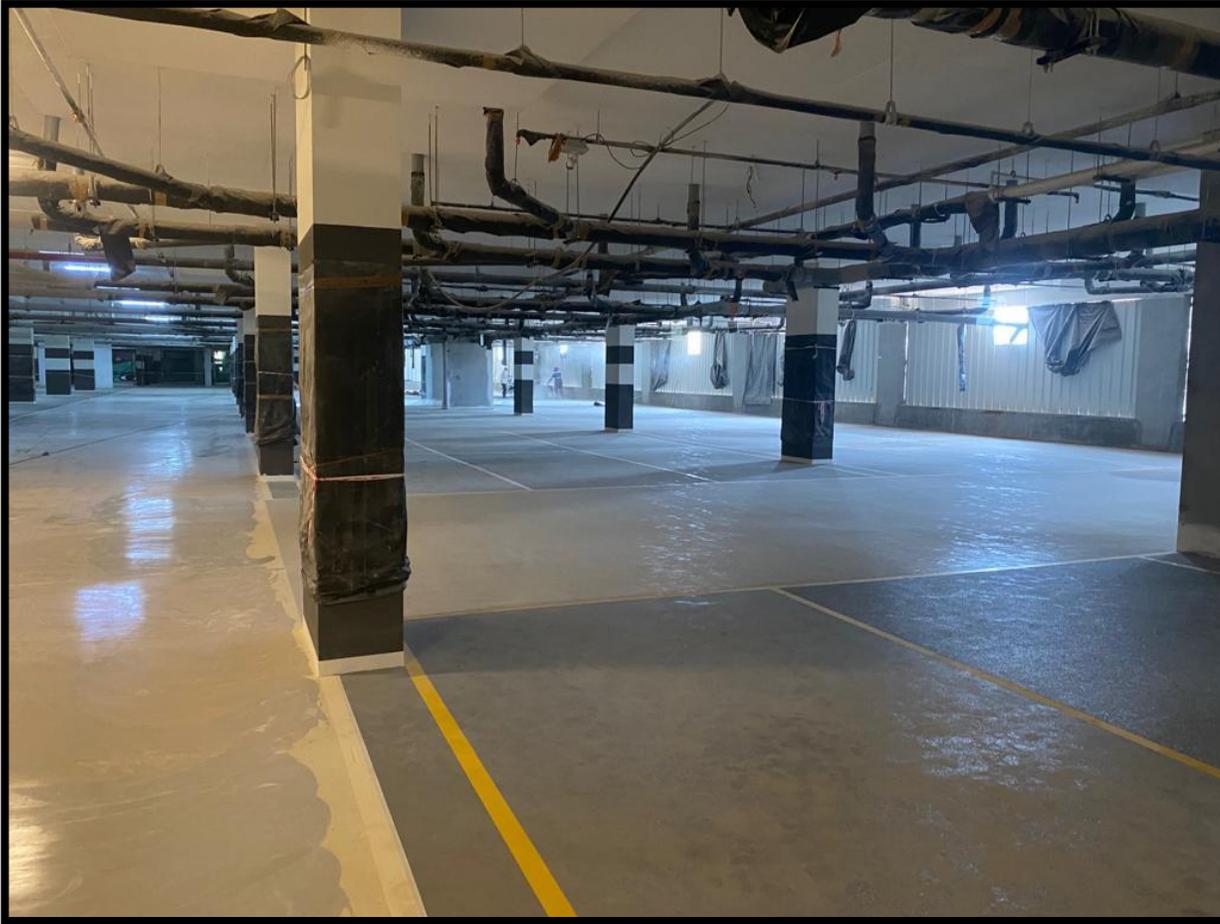


PU Flooring works

- **Primer ,Epoxy Coating Solutions and Top coat works in progress**



**Entrance gate structure completed. Blockwork completed.
Roof waterproofing & screed completed**

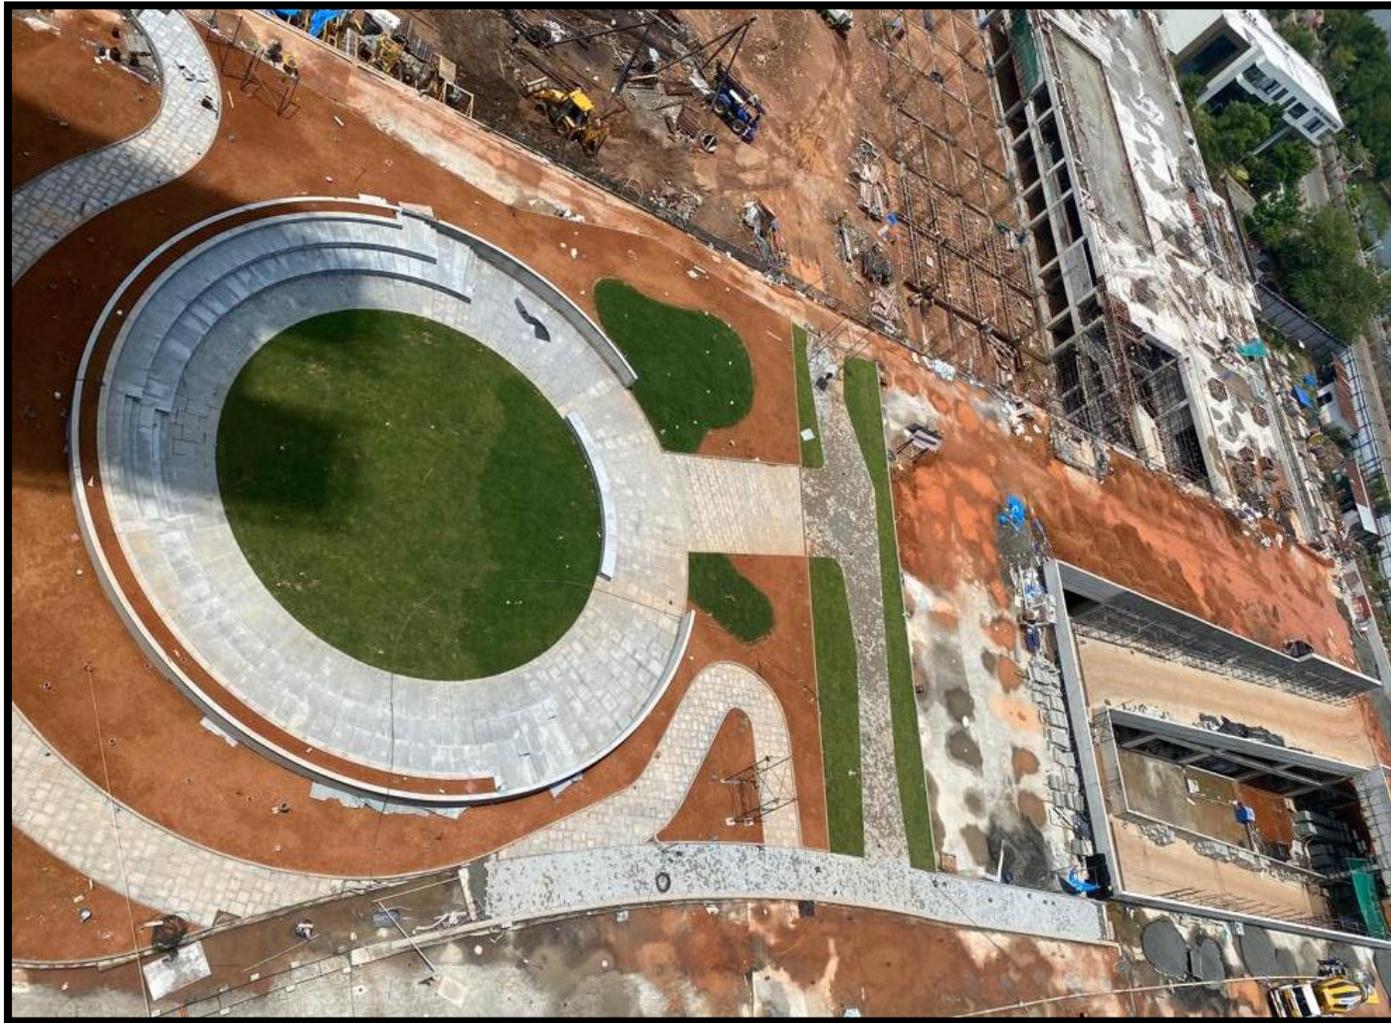

Podium kerb works & Paver works in progress. Amphitheatre granite works completed.


Podium area grass fixing completed. Soft landscaping works in progress.



Blockworks in progress



Backfilling completed. Grade slab works in progress

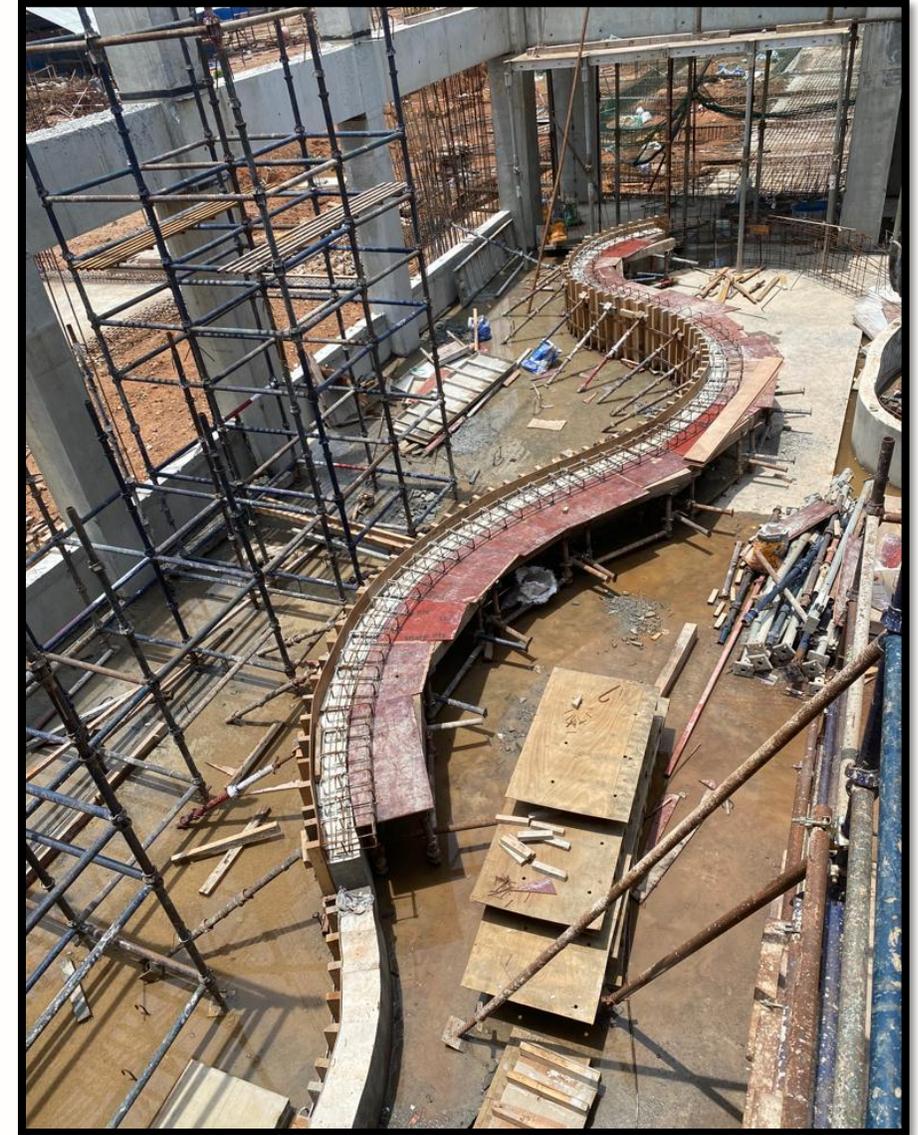

Seater wall works in progress

Thank You...
